



King County

Department of Natural Resources and Parks
Wastewater Treatment Division

Sewer Pipeline Work in Pacific, Algona & Auburn

Phase B of the Kent-Auburn Conveyance System Improvements Project

Construction Update – August 29, 2018

Upcoming pipe installation and restoration in Auburn, Algona, and Pacific


We are working to install and restore sewer pipes in Auburn, Algona, and Pacific. These improvements are needed to protect public health and the environment, allow us to continue providing safe, reliable sewer service, and provide enough capacity to transport wastewater into the future. Read below for the latest information about construction.

Upcoming work in Auburn

- **15th Avenue Southwest and Perimeter Road intersection:** following successful pipe installation, crews plan to grind and repave the road in early September
- **Perimeter Road:** over the next few weeks, crews will continue installing pipe along the west side of the road. Work is expected to continue through mid-September.

What to expect:

- **15th/Perimeter intersection work hours:**
 - Road preparation: Sept. 4-6 from 8:30 p.m. to 7 a.m.
 - Grinding and paving: Sept. 7-8 from 9:30 p.m. to 7 a.m.
- **Perimeter Rd. work hours:**
 - Through Aug. 31: 8:30 p.m. to 7 a.m. (night work)
 - Sept. 4–mid-Sept.: weekdays 7 a.m. to 7 p.m. (if necessary, crews will work Mon. to Sat. 7am to 10pm and Sunday 9am to 10pm)
- Temporary single lane closures as needed (signage and flaggers/uniformed police officers will direct drivers)
- Access to businesses will be maintained
- Large equipment, noise, and vibrations within approved limits

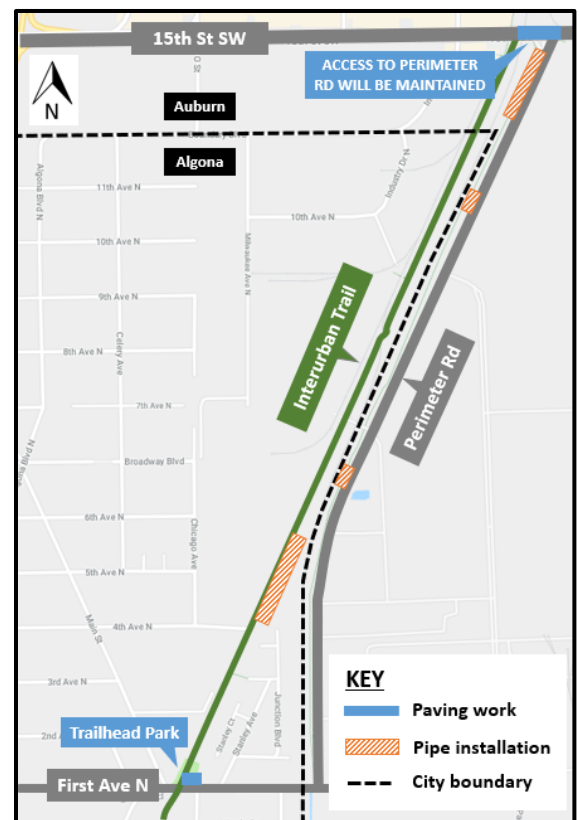

Map of upcoming construction in Auburn



An example of pipe installation

Upcoming work in Algona

- **Trailhead Park parking lot:** following successful pipe installation, crews plan to pave the parking lot as early as Sept. 8
- **Interurban Trail:** beginning as early as mid-Sept., crews will continue to install pipe just east of the Interurban Trail
- **Seattle Boulevard South:** over the next few weeks, crews will continue final restoration by intermittently working in and near manholes

What to expect:

- **Work hours:**
 - Parking lot paving: evening of Sept. 8, (exact time TBD)
 - Pipe installation and restoration: weekdays, 7:30 a.m. to 6 p.m.
- Restricted parking; please look out for no parking signs in work areas
- Access to businesses will be maintained
- Construction traffic entering and exiting First Avenue North
- Large equipment, noise, and vibrations within approved limits

Upcoming work in Pacific


- **Frontage Road restoration:** following successful paving earlier this summer, crews plan to replace some sidewalk panels and install curb ramps at locations along the road. This work will begin as early as August 31 and is expected to last less than a week.

What to expect:

- **Work hours:** weekdays, 7 a.m. to 7 p.m.
- Driveway and business access will be maintained
- Restricted parking; please look out for no parking signs
- The contractor will contact any individual businesses and residents who may be affected by the work
- No work is planned in the Ellingson Road intersection

For more information:

- Visit www.kingcounty.gov/kent-auburn-csi
- Call the project hotline at 206-205-9283
- Email David Freed at david.freed@kingcounty.gov

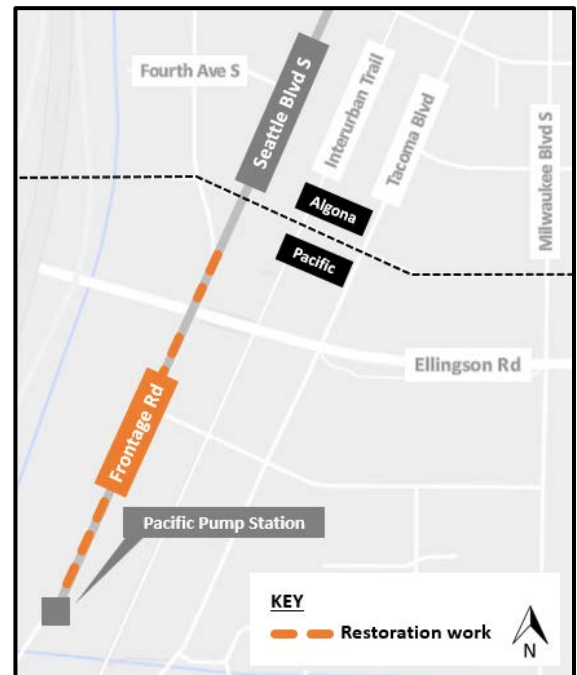

Map of upcoming construction in Pacific
