


King County Planning and engineering Services for the Master Plan for Resiliency and Recovery of King County’s Regional Wastewater Treatment Facilities  
November 14, 2016

FOURTH DRAFT FOR SCOPE/LOE DEVELOPMENT CONVERSATIONS – Page 1 of 3

Project Phase	November 2016	December	January	February	March	April 2017
		200.01 – Conduct Preliminary Evaluation		200.03 – Prepare for and Perform Field Inspections for High Risk Facilities		200.04 – Conduct Additional Desktop Evaluation, Prioritize, and Conduct Workshops >>>
			200.02 – Conduct Desktop Risk Assessment and Conduct Review Workshop			
		200.02(f) – Develop Criteria for Prioritization	200.02(g) – Prioritize Facilities for Further Evaluation 200.02(h) – Prioritize Pipelines for Further Evaluation	200.02(i) – Evaluate Additional Information for High- and Medium-Risk Assets	200.03(a-f) – Prepare for Field Work 200.03(g) – Conduct Field Inspections (treatment plants) 200.03(g) – Conduct Field Inspections (pump stations, regulator stations, CSO facilities)	200.04(a-b) – Conduct Additional Evaluation and ID High Risks
		300.01(a) – Conduct Desk-top Evaluation of Digesters	300.01(b) Prepare for Field Work	300.01(c-i) Conduct Field Work	300.02 Prepare Draft and Final Digester Technical Memorandum (Condition Report)	
Workshops/Meetings		200.01(e) Kick-off Meeting	300.01(b) Field Assessment Safety and Data Collection Meeting	200.02(k) Desktop Assessment Review Workshop 200.03(d) – Field Assessment Training		300.02(b) Technical Memorandum Review Meeting
Deliverables		Task 100 Draft Project Management Plan	Task 100 Final Project Management Plan Task 300 – Updated Field Safety Plan for Task 300	Task 200 Summary of Desktop Assessment Results Task 200 – Updated Field Safety Plan for Task 200	Task 300 Draft Digester Technical Memorandum (Condition Report)	Task 300 Final Digester Technical Memorandum (Condition Report)

King County Planning and engineering Services for the Master Plan for Resiliency and Recovery of King County’s Regional Wastewater Treatment Facilities  
November 14, 2016

FOURTH DRAFT FOR SCOPE/LOE DEVELOPMENT CONVERSATIONS – Page 2 of 3

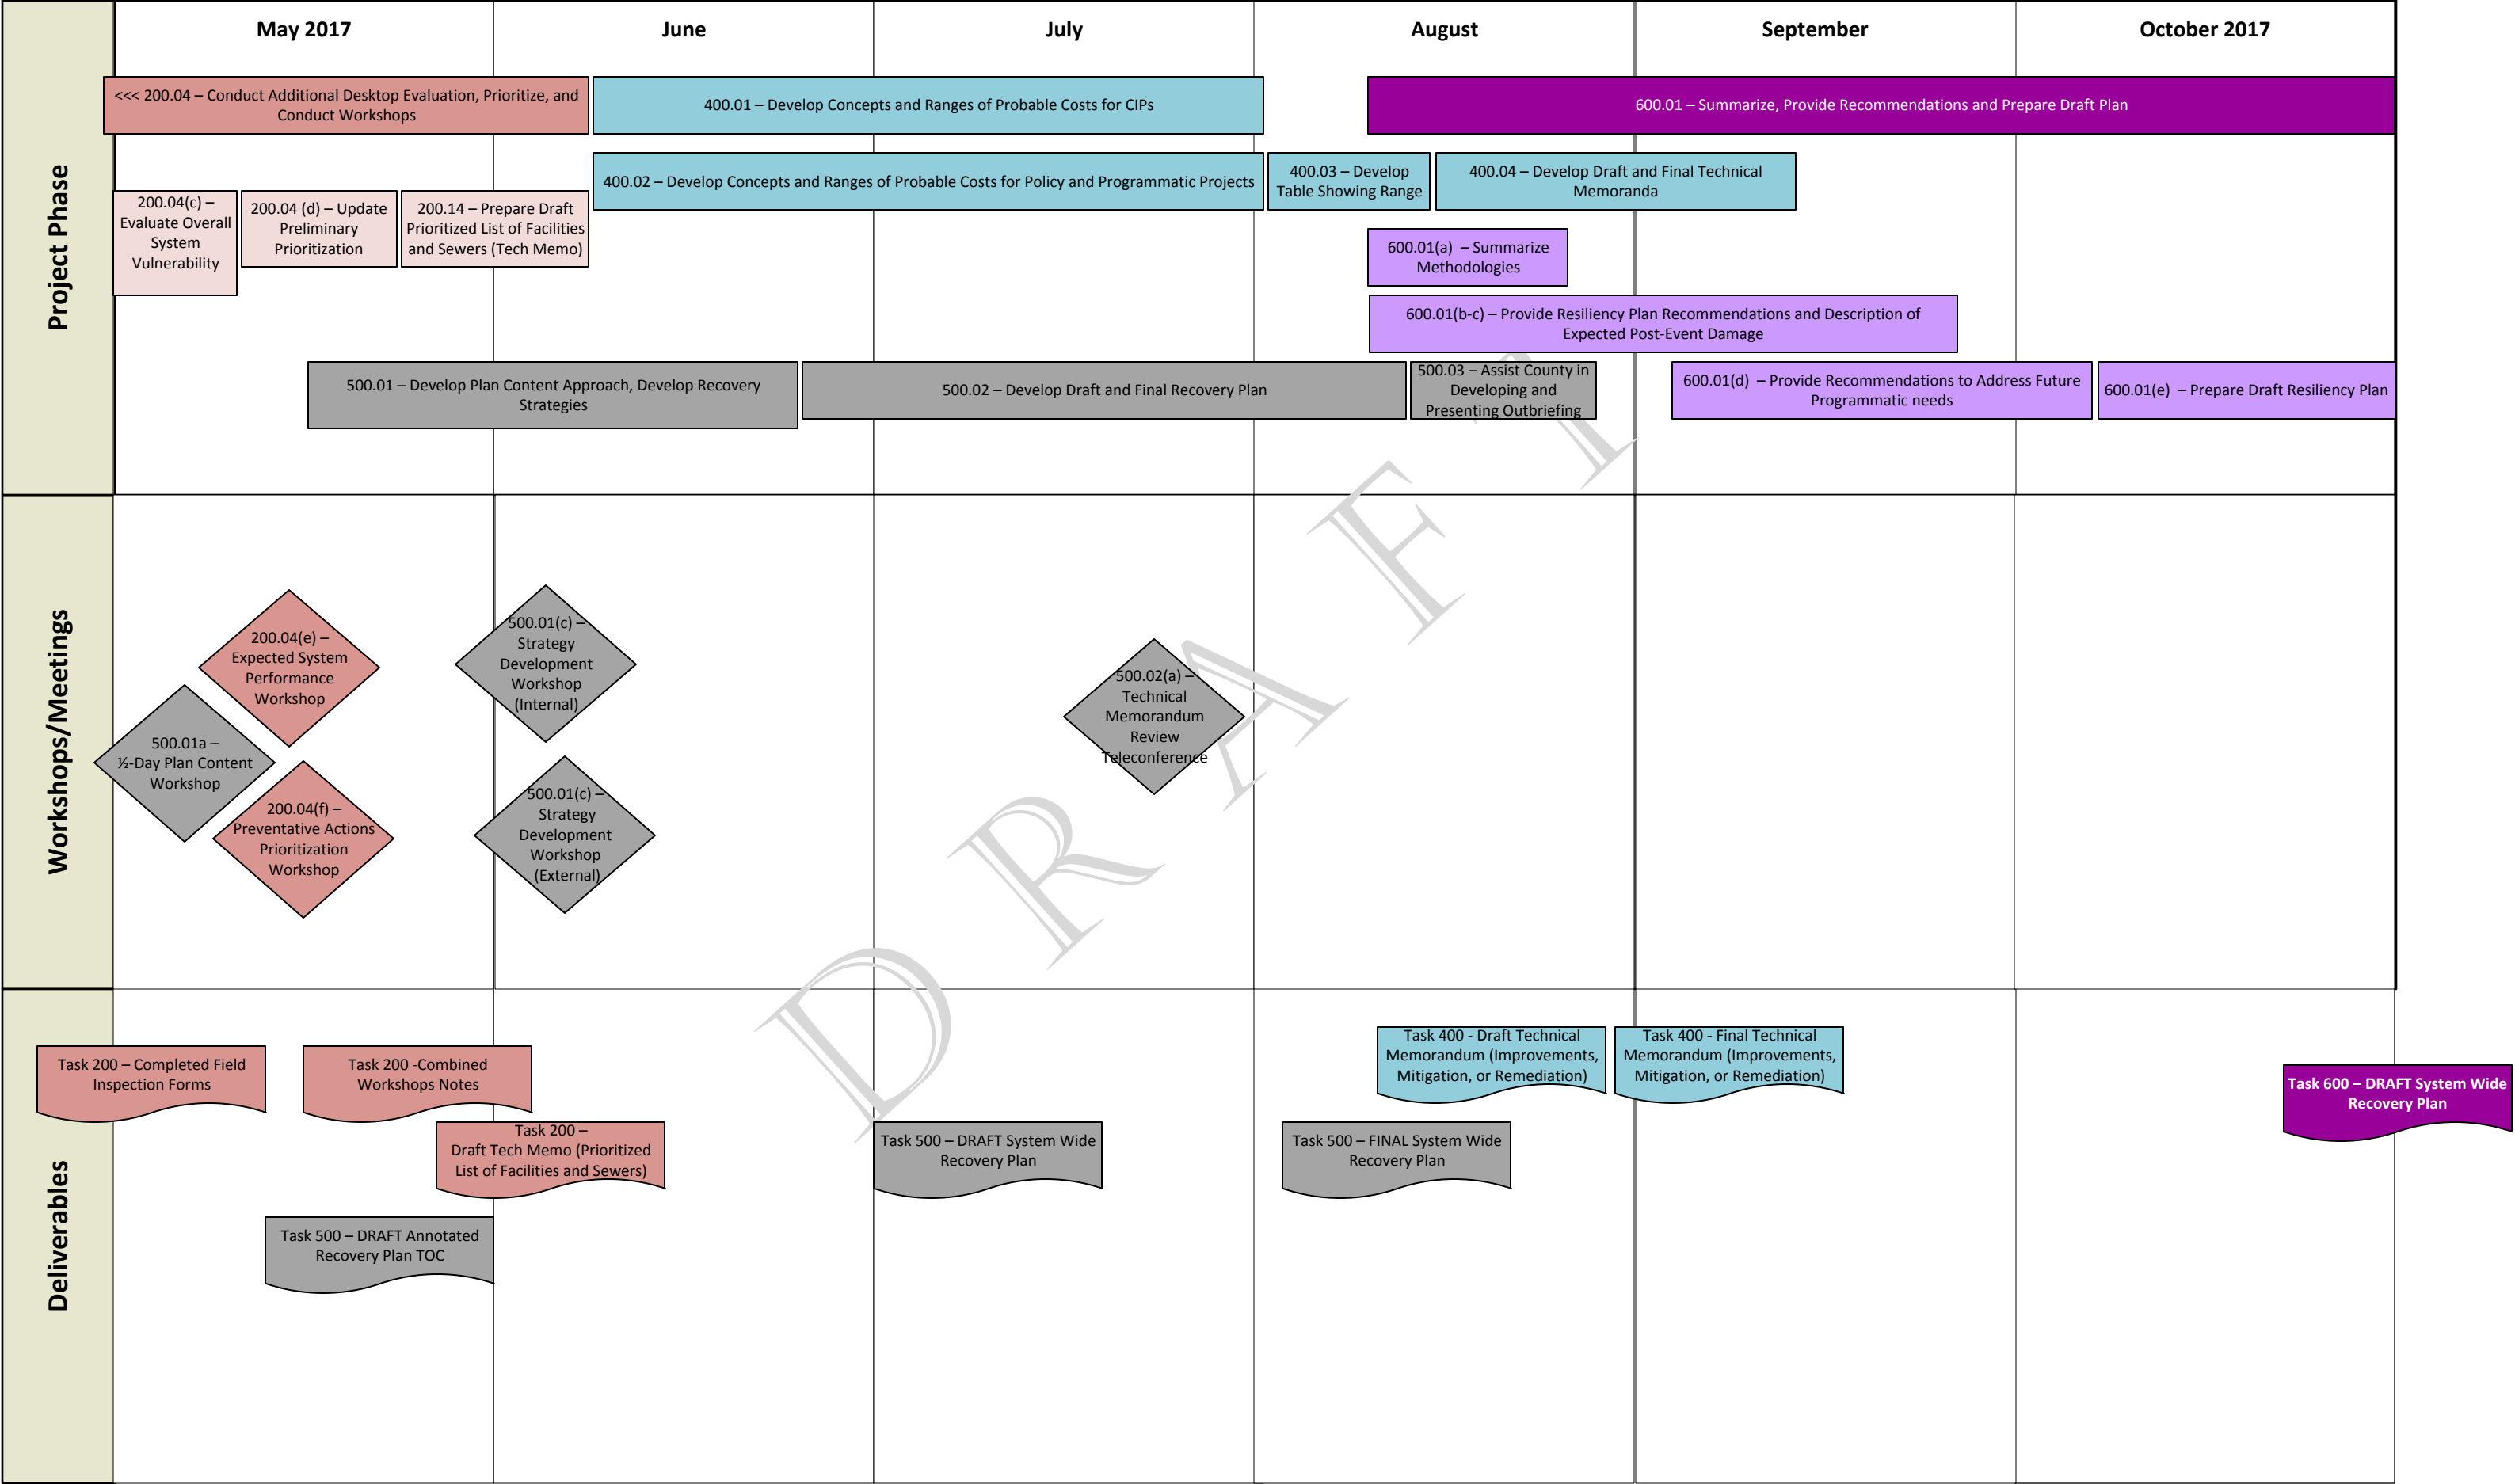

Project Phase	November 2017	December 2017	January 2018			
	<div>600.02 – Assist County in Mid-Point Briefing</div>	<div>600.03 – Prepare Final Final Resiliency Plan</div>				
Workshops/Meetings						
Deliverables		<div>Task 600 – FINAL System Wide Recovery Plan</div> <div>Task 600– PPT Slides</div>				
